**N O T E**

If the slide show is not launched, click on **View → Slide Show** in the menu bar at the top of the Power Point window.

When the **View** option is not visible, the slide show has been launched and you must click to proceed to the next slide.

PMT 250
Program Management
Tools Course

*"CLICK" TO CONTINUE…*

# RISK MANAGEMENT PROCESS FLOW

PMT 250
Program Management
Tools Course

*"CLICK" TO CONTINUE…*

# Risk Management Process

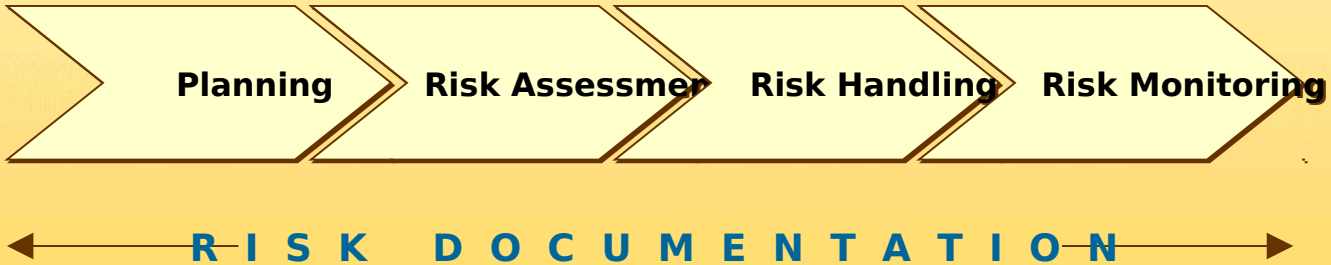


PMT 250
Program Management
Tools Course

"CLICK" TO CONTINUE...

# Risk Planning

Develop an organized, comprehensive and interactive strategy and methods for identifying and tracking risk management activity.

- Assign adequate resources to manage risk
- Develop a risk management strategy and approach
- Train IPT personnel in risk management techniques
- Draft a risk management plan which provides a process to manage risk



"CLICK" TO CONTINUE...

# Risk Assessment

- Identify and analyze risk events in order to rate…
- Includes **Risk Identification** and **Risk Analysis** Sub-Processes

"CLICK" TO CONTINUE…

# Risk Identification

- Examine the program areas and each critical technical component to identify and document associated risk.

"CLICK" TO CONTINUE...

# Risk Analysis

- Examine identified risks, isolate causes, determine the relationship to other risks, express the risk rating (high, medium, low) based on probability and consequences, and prioritize risks in a "watch" list.
  - Items on the risk "watch" list become prime candidates for identification as "exit criteria", which are critical program results
  - Exit criteria for the following phase are identified in the a acquisition

"CLICK" TO CONTINUE...

# Risk Handling

- Identify, evaluate, select, and implement options in order to set risk at acceptable levels given program constraints and objectives.
  - Specifics on what should be done
  - When it should be accomplished
  - Who is responsible
  - Associated cost

"CLICK" TO CONTINUE...

# Risk Monitoring

- Systematically track and evaluate the performance of risk-handling actions against established metrics throughout the acquisition process
- Results may also provide a basis for developing additional handling options and identifying new risks.

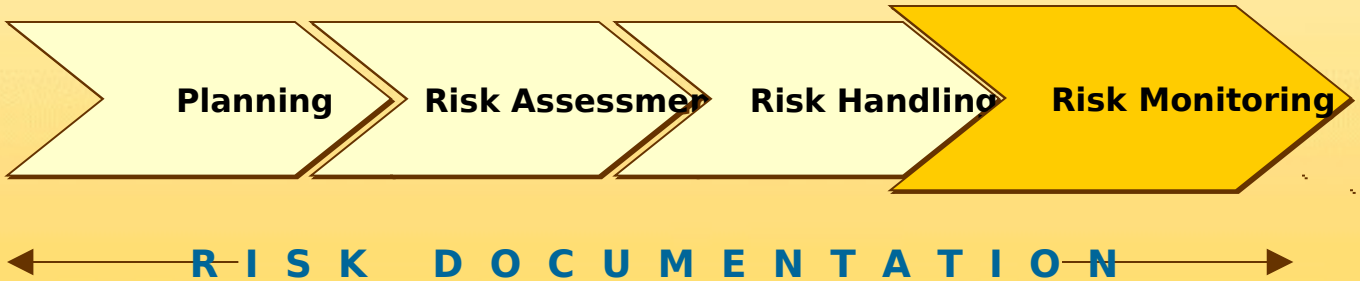




"CLICK" TO CONTINUE...

# Risk Documentation

- Record, maintain and report assessments, handling analysis, plans, and the results of monitoring
- Provides the basis for reporting risk and overall program information,
  both internally and externally
- Done throughout each phase in the risk management process

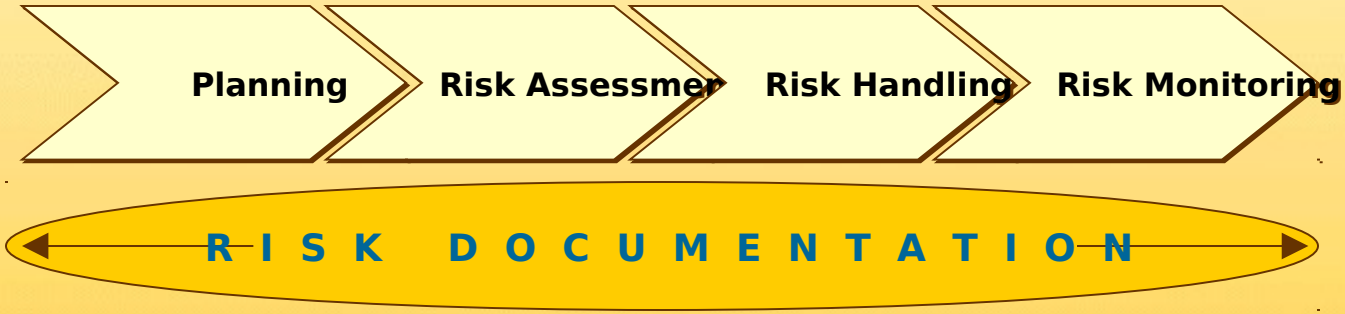




"CLICK" TO CONTINUE...

**SAMPLE**

To print the PowerPoint slides, click on **File → Print...**
You will then be prompted to choose your print options. Select them and click **OK**

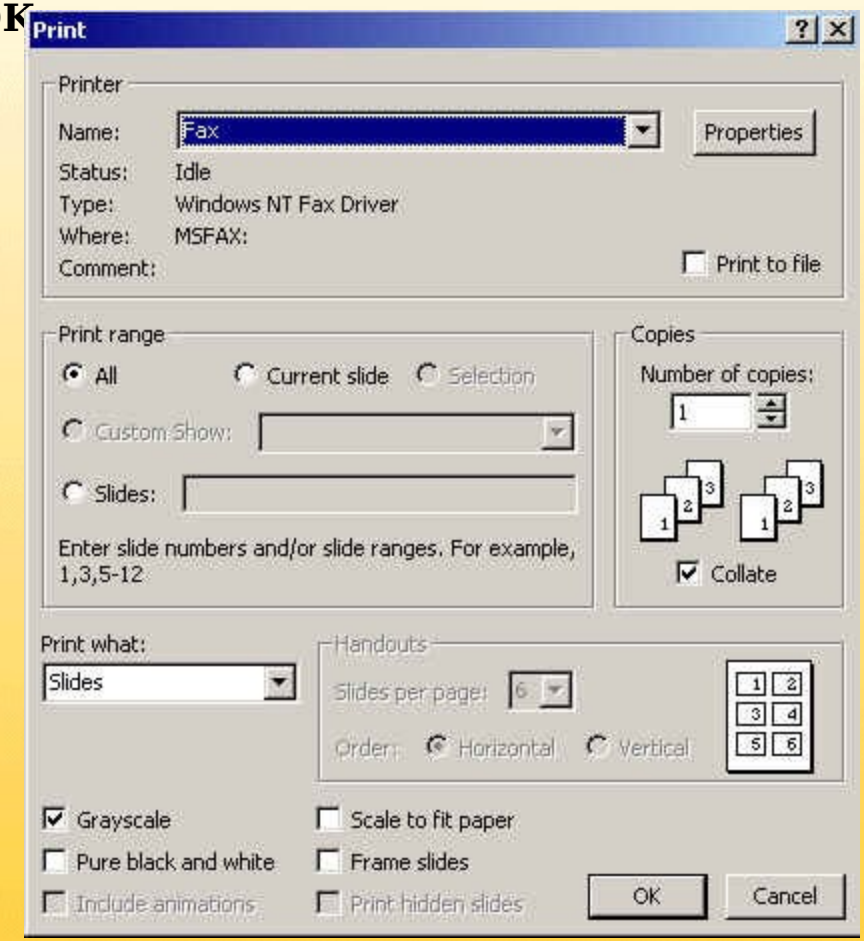


PMT 250
Program Management
Tools Course
